




Project: case 2
Date: Wed 03-06-09

Task

Split

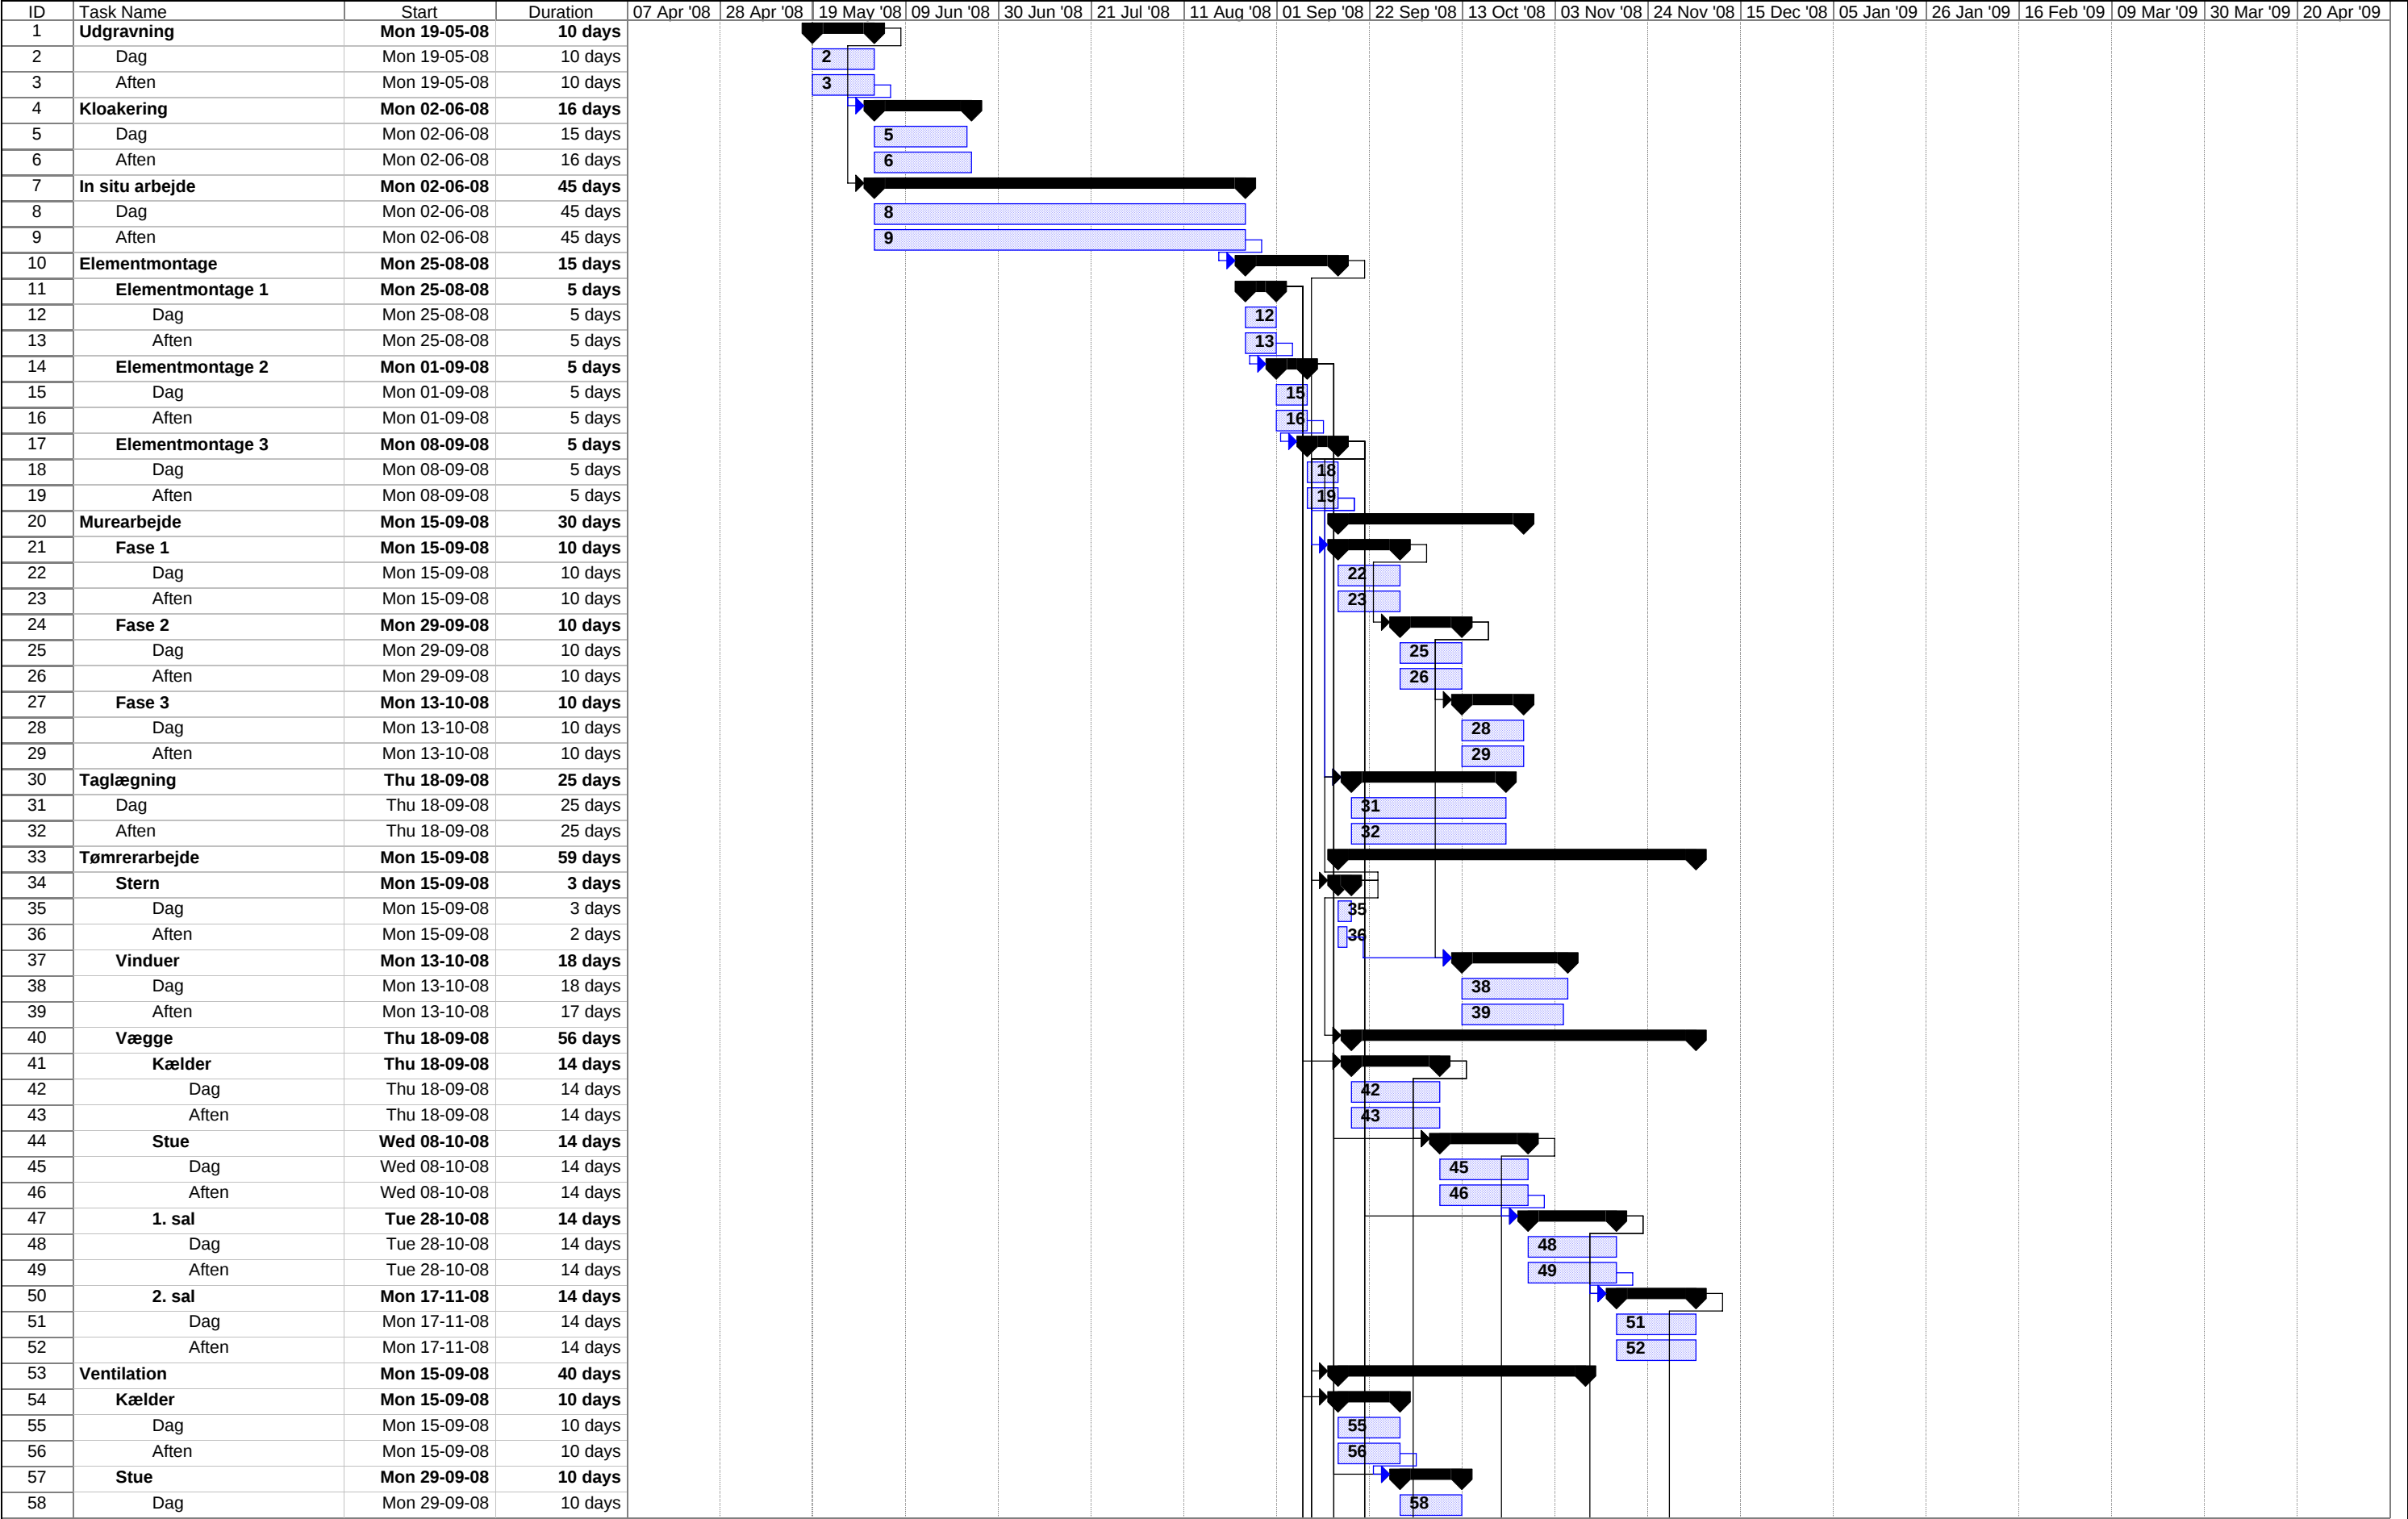

Progress

Milestone



Summary

Project Summary




External Tasks

External Milestone



Deadline



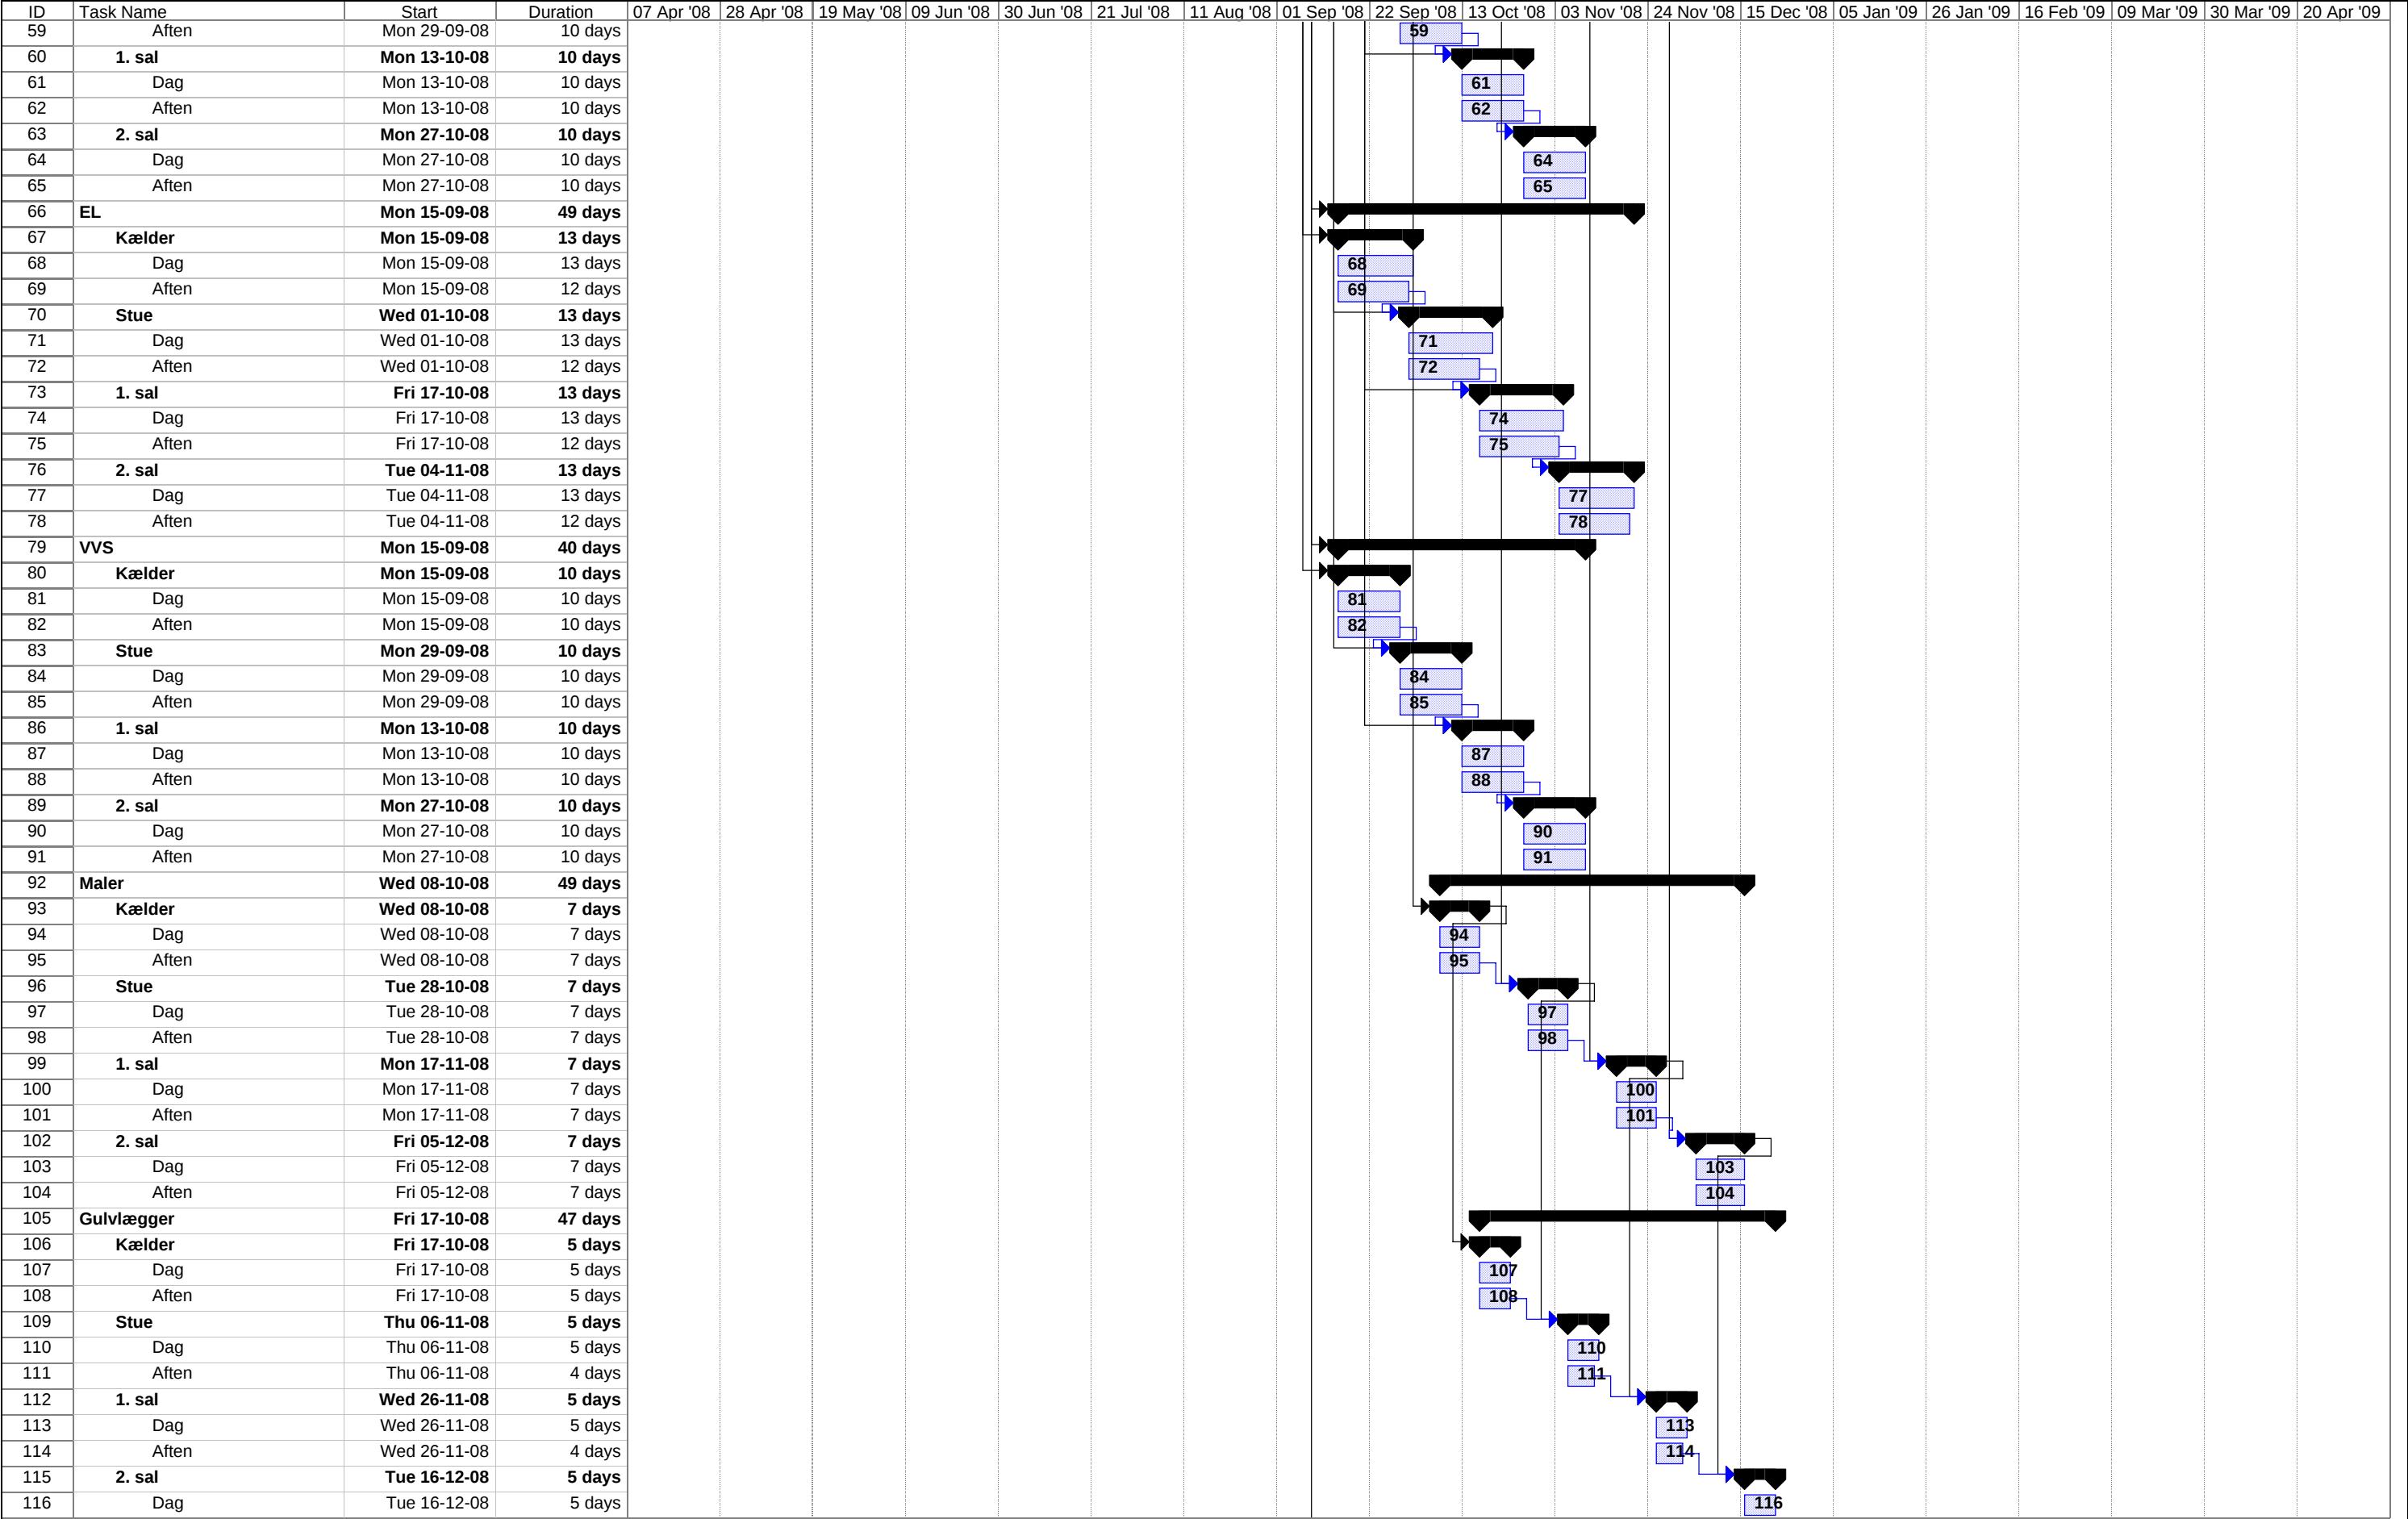

Project: case 2
Date: Wed 03-06-09

Task



Progress



Summary



External Tasks



Deadline



Split



Milestone



Project Summary



External Milestone



ID	Task Name	Start	Duration	07 Apr '08	28 Apr '08	19 May '08	09 Jun '08	30 Jun '08	21 Jul '08	11 Aug '08	01 Sep '08	22 Sep '08	13 Oct '08	03 Nov '08	24 Nov '08	15 Dec '08	05 Jan '09	26 Jan '09	16 Feb '09	09 Mar '09	30 Mar '09	20 Apr '09
117	Aften	Tue 16-12-08	4 days													117						
118																						
119	Udgravning: P-hus	Mon 15-09-08	25 days																			
120	Dag	Mon 15-09-08	25 days																			
121	Aften	Mon 15-09-08	25 days																			
122	Kloakering: P-hus	Mon 20-10-08	6 days																			
123	Dag	Mon 20-10-08	6 days																			
124	Aften	Mon 20-10-08	5 days																			
125	In situ arbejde: P-hus	Mon 20-10-08	10 days																			
126	Dag	Mon 20-10-08	10 days																			
127	Aften	Mon 20-10-08	10 days																			
128	Elementmontage: P-hus	Mon 03-11-08	10 days																			
129	Dag	Mon 03-11-08	10 days																			
130	Aften	Mon 03-11-08	10 days																			
131	VVS: P-hus	Mon 17-11-08	5 days																			
132	Dag	Mon 17-11-08	5 days																			
133	Aften	Mon 17-11-08	5 days																			
134	EL: P-hus	Mon 17-11-08	5 days																			
135	Dag	Mon 17-11-08	5 days																			
136	Aften	Mon 17-11-08	5 days																			
137	Ventilation: P-hus	Mon 17-11-08	5 days																			
138	Dag	Mon 17-11-08	5 days																			
139	Aften	Mon 17-11-08	5 days																			



Project: case 2
Date: Wed 03-06-09

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline
